

SOFTWARE ENGINEERING

LAB 2

Agile Backlog Creation & Sprint Simulation in Jira

Digital Art Commission & Watermarking Portal (DACWP)

NAME : SUMAN DIDDIMANI

SRN : PES1UG24AM409

SECTION : G

1. Objective

Use Jira to turn functional requirements into Agile backlog items, simulate a sprint, and analyse progress. Lab 1 functional requirements are converted into Epics and User Stories, prioritized, estimated, and used to run a mini-sprint.

2. EPICS AND USER STORIES

User Stories follow the format: As a [user role], I want [goal], so that [benefit].

Epic 1: Commission Request & Management

Description: Enables clients to submit creative briefs and manage the commission process, including accepting commissions, defining milestones, and establishing the initial requirements for the artwork.

User Story	Description	Priority	Story Points
Submit Creative Brief	As a Client Buyer, I want to submit a creative brief containing scope, reference images, dimensions, file-format needs, deadline, budget, and milestone terms, so that the commission requirements are clearly defined.	High	5
Accept Commission & Define Milestones	As an assigned Digital Artist, I want to accept a commission and define the agreed milestones, so that the work can proceed with clear deliverables and milestones.	High	5
Upload Versioned WIP Draft	As a Digital Artist, I want to upload versioned WIP drafts against an open milestone, so that the client can review progress while the original remains protected.	High	5

Epic Total Story Points: 15

Epic 2: WIP Draft Protection & Review

Description: Enables Digital Artists to protect unfinished artwork with dynamic watermarking and allows Client Buyers to review WIP drafts, provide feedback, request revisions, or approve milestones.

User Story	Description	Priority	Story Points
Apply Dynamic Watermark	As a Digital Artist, I want every WIP draft to receive a dynamic diagonal watermark containing the commission ID and buyer identifier before it is shown to the client, so that unfinished artwork is protected from unauthorized use.	High	8
Review WIP & Provide Feedback	As a Client Buyer, I want to review a watermarked WIP draft and provide contextual feedback, so that the artist understands the changes required.	High	8
Request Revision or Approve Milestone	As a Client Buyer, I want to request a revision or approve the associated milestone, so that the WIP review process has a clear outcome.	High	5

Epic Total Story Points: 21

Epic 3: Payment & Final Asset Delivery

Description: Enables secure milestone payment verification and ensures that final high-resolution artwork is released to the Client Buyer only after successful payment, with secure access to the final asset.

User Story	Description	Priority	Story Points
Verify Milestone Payment	As a Client Buyer, I want my milestone payment to be verified successfully, so that the system can authorize access to the final high-resolution asset.	High	8
Unlock Final High-Resolution Asset	As a Client Buyer, I want the final high-resolution source file to be unlocked only after successful milestone payment verification, so that I receive the final artwork after completing the required payment.	High	8
Secure Final Asset Download	As a Client Buyer, I want to download the final asset through a secure signed URL, so that unauthorized users cannot access the file.	High	8

Epic Total Story Points: 24

Epic 4: Audit & Platform Reliability

Description: Ensures the platform remains reliably available and maintains immutable audit records for important commission activities, providing dependable collaboration and evidence for resolving disputes.

User Story	Description	Priority	Story Points
Maintain Platform Availability	As a platform user, I want the portal to maintain reliable availability, so that I can access commission	Medium	5

	management and asset delivery services when needed.		
Maintain Immutable Audit Records	As a platform administrator, I want immutable audit records for brief, draft, approval, payment, and download actions to be retained for 365 days, so that important activities can be traced when resolving disputes.	Medium	5

Epic Total Story Points: 10

3. STORY POINT ASSIGNMENTS

Story Points use the Fibonacci sequence and represent relative effort, complexity, time, risk, and uncertainty.

Epic	Stories	Assignments	Total
Epic 1	3	5 + 5 + 5	15
Epic 2	3	8 + 8 + 5	21
Epic 3	3	8 + 8 + 8	24
Epic 4	2	5 + 5	10
TOTAL	11		70

Jira Backlog showing all Epics, User Stories, priorities, and Story Points.

Spaces / Digital Art Commission & Watermarking Portal

DACWP board

Summary List Active sprints **Backlog** Calendar Timeline Docs Forms Development

Search backlog Version Epic Quick filters

Epic

- No epic
- Commission Request & Management
- WIP Draft Protection & Review
- Payment & Final Asset Delivery
- Audit & Platform Reliability

Stories:

- DACWP-2 Submit Creative Brief (Commission Request & Management, 5 points)
- DACWP-3 Accept Commission & Define Milestones (Commission Request & Management, 5 points)
- DACWP-4 Upload Versioned WIP Draft (Commission Request & Management, 5 points)
- DACWP-6 Apply Dynamic Watermark (WIP Draft Protection & Review, 8 points)
- DACWP-7 Review WIP & Provide Feedback (WIP Draft Protection & Review, 8 points)
- DACWP-8 Request Revision or Approve Milestone (WIP Draft Protection & Review, 5 points)
- DACWP-10 Verify Milestone Payment (Payment & Final Asset Delivery, 8 points)
- DACWP-11 Unlock Final High-Resolution Asset (Payment & Final Asset Delivery, 8 points)
- DACWP-12 Secure Final Asset Download (Payment & Final Asset Delivery, 8 points)
- DACWP-14 Maintain Platform Availability (Audit & Platform Reliability, 5 points)
- DACWP-15 Maintain Immutable Audit Records (Audit & Platform Reliability, 5 points)


4. SPRINT 1

Sprint Goal: Complete the core commission request and WIP review workflow, including creative brief submission, milestone definition, versioned WIP draft upload, watermarking, and client feedback/approval.

Duration: 1 week | Planned Stories: 6 | Planned Story Points: 36

Story	Story Points	Progress Flow
Submit Creative Brief	5	To Do → In Progress → Done
Accept Commission & Define Milestones	5	To Do → In Progress → Done
Upload Versioned WIP Draft	5	To Do → In Progress → Done
Apply Dynamic Watermark	8	To Do → In Progress → Done
Review WIP & Provide Feedback	8	To Do → In Progress → Done
Request Revision or Approve Milestone	5	To Do → In Progress → Done

Sprint 1 Active Sprint Board showing the six stories and their progress.

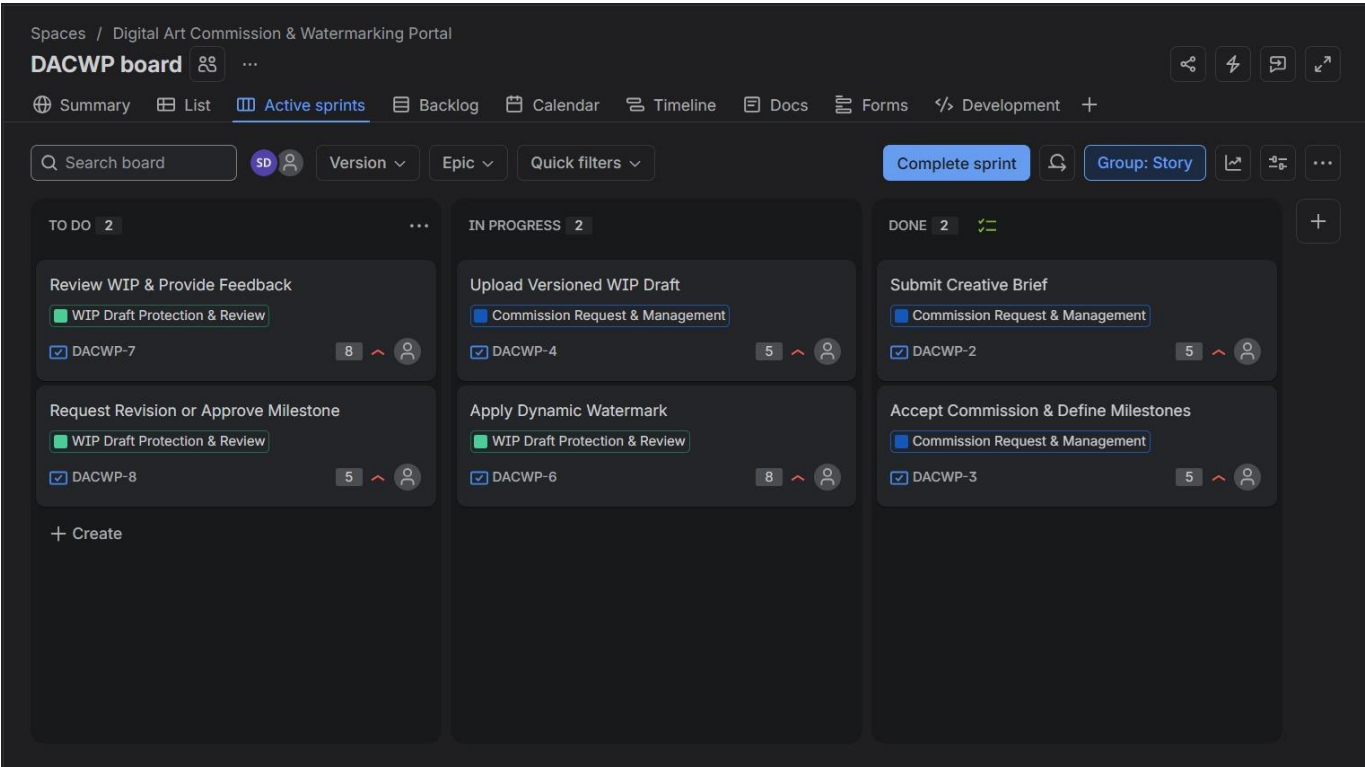


5. SPRINT 2

Sprint Goal: Complete secure payment verification, final high-resolution asset delivery, secure asset download, platform availability, and immutable audit record management.

Duration: 1 week | Planned Stories: 5 | Planned Story Points: 34

Story	Story Points	Progress Flow
Verify Milestone Payment	8	To Do → In Progress → Done
Unlock Final High-Resolution Asset	8	To Do → In Progress → Done
Secure Final Asset Download	8	To Do → In Progress → Done
Maintain Platform Availability	5	To Do → In Progress → Done
Maintain Immutable Audit Records	5	To Do → In Progress → Done

Sprint 2 Active Sprint Board showing the five stories and their progress.

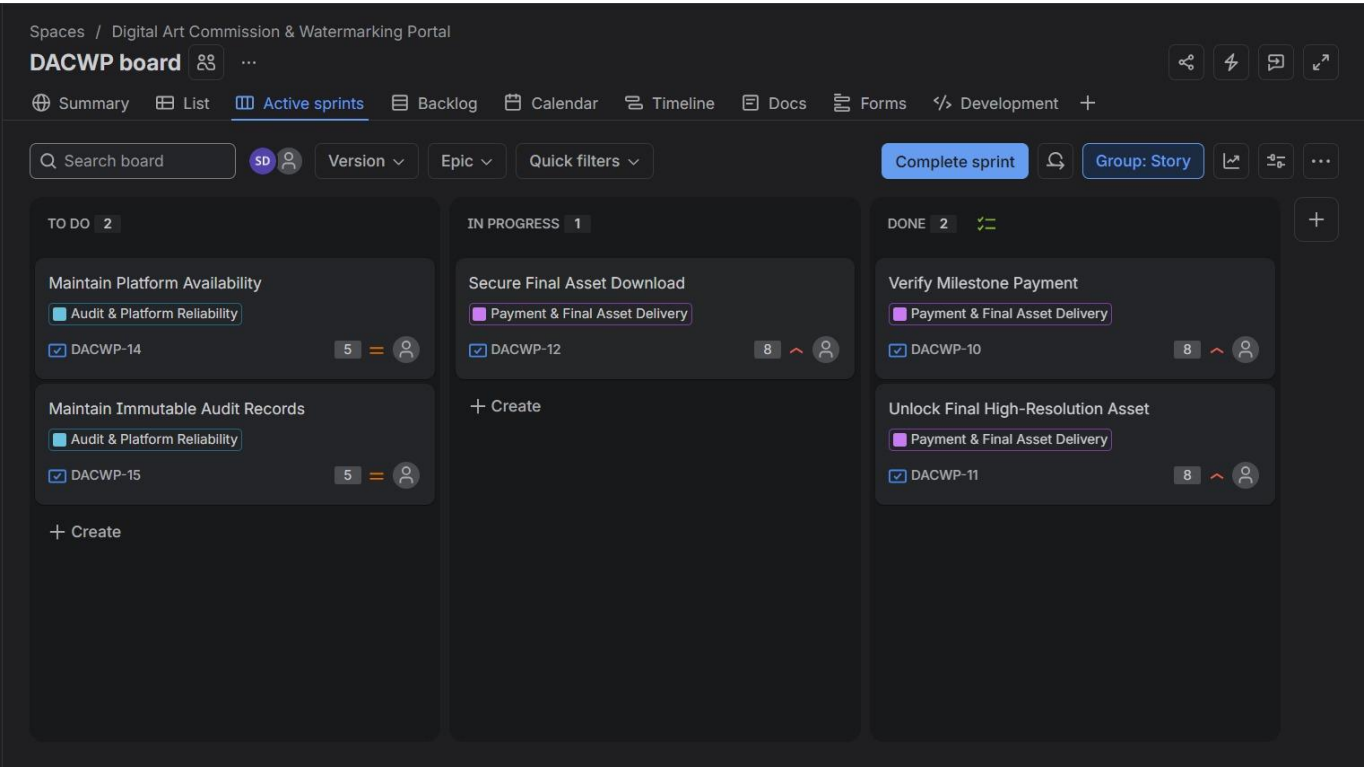


6. BURNDOWN CHART

Go to Reports → Burndown Chart. Observe how Story Points are completed across the sprint and reflect on delays, early completions, or inconsistencies.

Sprint 1: 36 Story Points planned → 0 remaining.


Sprint 1 Burndown Chart.

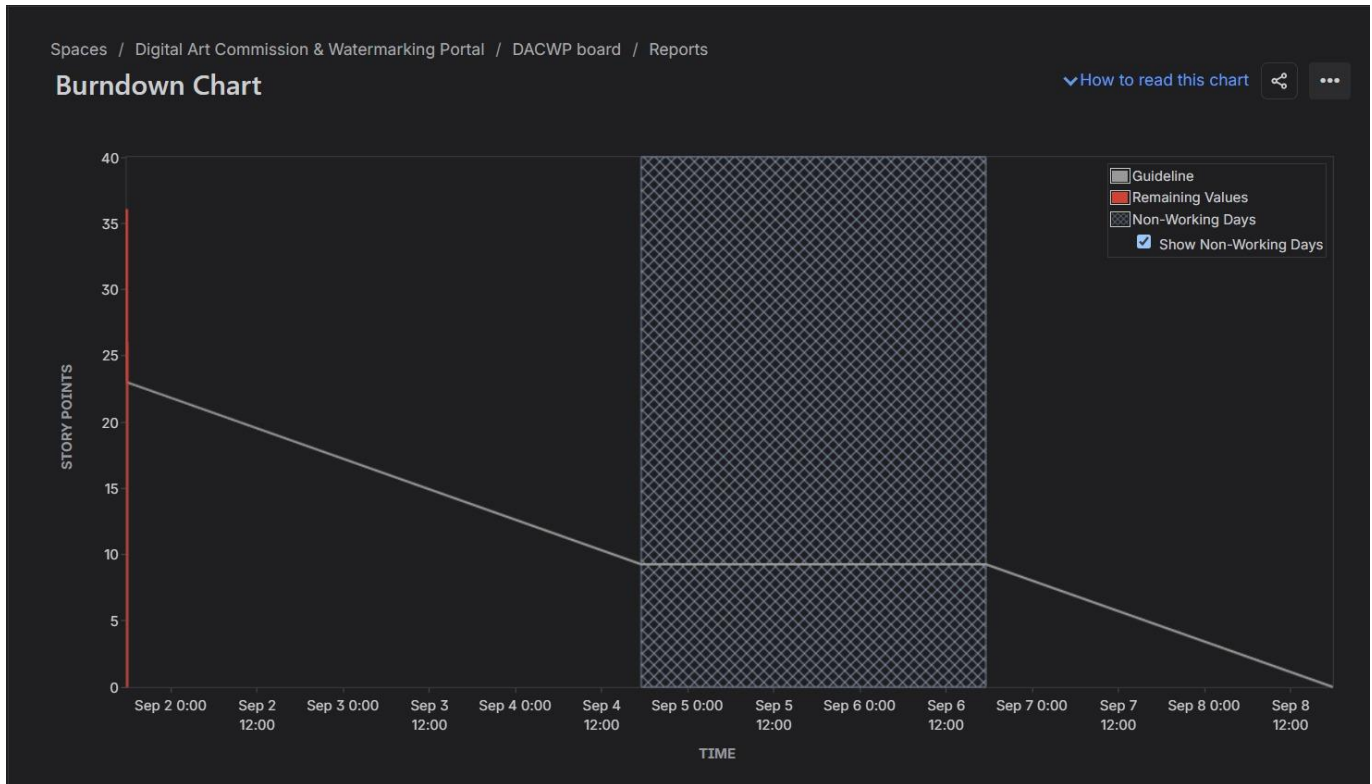

Sprint 2: 34 Story Points planned → 0 remaining.

Sprint 2 Burndown Chart.

Burndown Chart

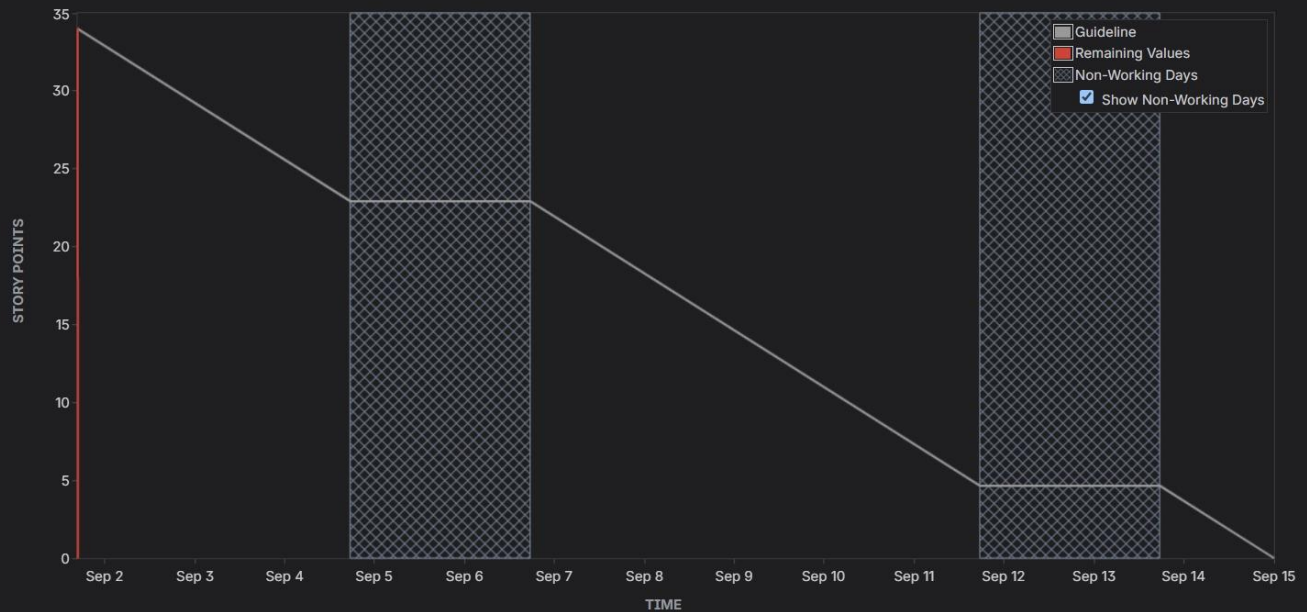[How to read this chart](#)

7. REFLECTION QUESTIONS

1. Did your estimations reflect the actual effort?

Yes. The Story Point estimates provided a consistent relative measure of planned work. Sprint 1 completed 36 Story Points and Sprint 2 completed 34 Story Points, so all planned work was completed.

2. Was your backlog well-prioritized?

Yes. The backlog was organized around the main workflow and prioritized according to user impact. Sprint 1 focused on commission request and WIP review, while Sprint 2 focused on payment, final asset delivery, and reliability.

3. How did your simulated sprint align with your plan?

The simulated sprints aligned with the plan because the selected User Stories were moved through To Do, In Progress, and Done, and both sprints were completed within their one-week time boxes.

4. What insights did the burndown chart give about your team's capacity?

The Burndown Charts showed that the planned workload could be completed within the sprint time boxes. The simulation completed 70 Story Points across two sprints: 36 in Sprint 1 and 34 in Sprint 2.
